FitMe - Product Roadmap

Team mission


Empower people to take control of their health by building FitMe, an intuitive mobile fitness app that makes it easy to log workouts, track nutrition, monitor daily activity, and stay motivated through personalized insights and social accountability. We ship iteratively, measure ruthlessly, and launch a polished GA product by September 2026.

🔗 Project information

Field	Detail
Timeline	May 5 – Sep 3, 2026 (8 sprints, 4 phases)
GA target	September 3, 2026
Product Owner	Daniel Park
Scrum Master	Alexey Kim
Developer	Derrick Xie
QA Engineer	Haneef Abdur-Rasheed

Roadmap Overview

The FitMe roadmap is organized into four phases across 8 two-week sprints (May–September 2026). Phase 1 establishes core onboarding and manual data logging. Phase 2 introduces social and engagement features to drive retention. Phase 3 deepens nutrition insights and polishes the user experience. Phase 4 hardens the product for beta and public GA launch.

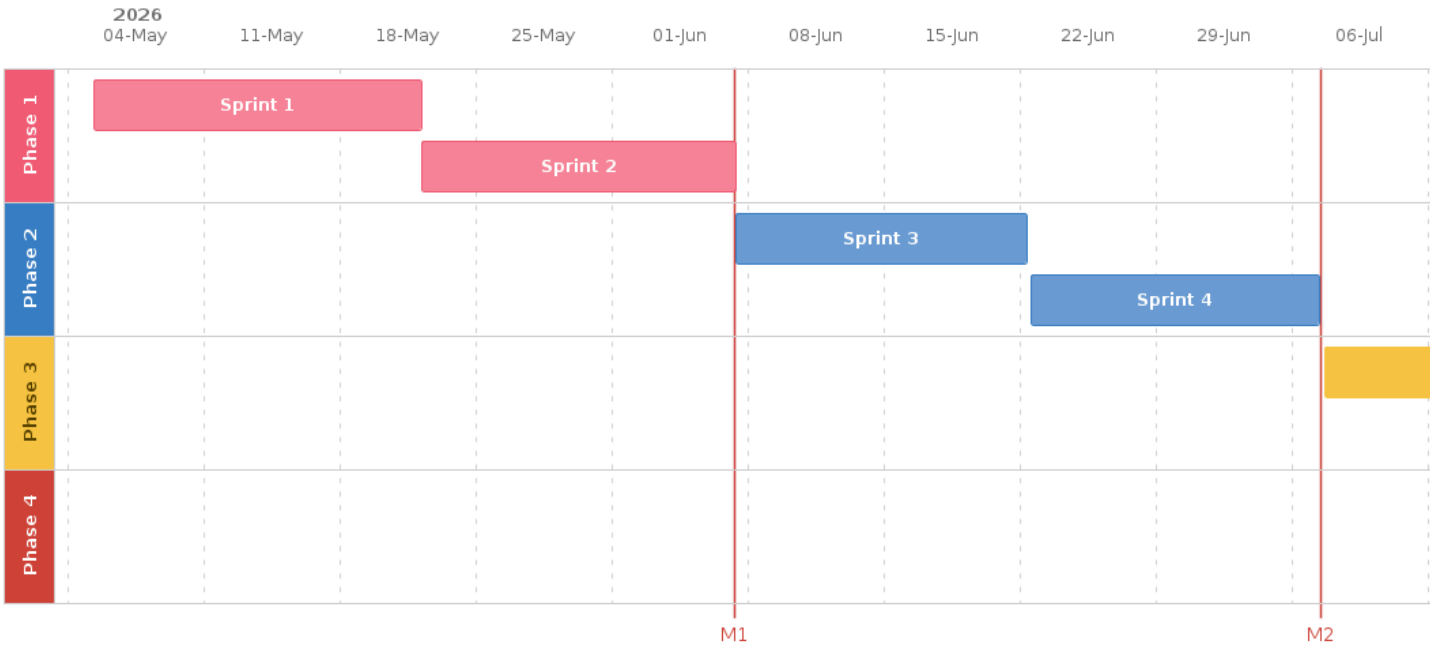

Phases, Sprints, and Milestones

Phase 1 — Foundations and Core Functionality

Objective: Deliver core onboarding and manual logging, establish performance baselines.

- **Sprint 1:** `May 5, 2026` – `May 19, 2026`
  Focus: Establish Core User Onboarding and Manual Data Logging.
  Indicative scope: User Registration, Profile Setup, Workout Logging, Step Tracking, Calorie Counter, Progress Dashboard.
- **Sprint 2:** `May 20, 2026` – `Jun 3, 2026`
  Focus: Deepen User Retention via Notifications & Utility.
  Indicative scope: Goal Setting, Core utilities, performance tuning, instrumentation.

Milestones:

- **M1:** Core onboarding live with logging + retention enablers (goals & notifications) shipped with baseline metrics (`Jun 3, 2026`)

Phase 2 — Engagement and Social Features

Objective: Introduce social and competitive features to drive engagement loops.

- **Sprint 3:** `Jun 4, 2026` – `Jun 18, 2026`
  Focus: Social Sharing, Accessibility features; refine analytics funnels.

- **Sprint 4:** `Jun 19, 2026` – `Jul 3, 2026`
  Focus: Tips and recommendations, experiment with social invites and re-engagement triggers.

Milestones:

- **M2:** Social engagement loops validated + leaderboard adoption driving retention uplift (`Jul 3, 2026`)

Phase 3 — Depth and Insights

Objective: Expand depth with nutrition insights and habit reinforcement.

- **Sprint 5:** `Jul 6, 2026` – `Jul 20, 2026`
  Focus: AI Analysis of tracked data; dashboard insight cards; goals adherence nudges.
- **Sprint 6:** `Jul 21, 2026` – `Aug 4, 2026`
  Focus: Personalization improvements; performance p95 checks; accessibility polish.

Milestones:

- **M3:** Macro insights live with adoption targets met + experience health and accessibility targets achieved (`Aug 4, 2026`)

Phase 4 — Scale, Quality, and Launch Readiness

Objective: Harden, localize, and prepare for broader release.

- **Sprint 7:** `Aug 5, 2026` – `Aug 19, 2026`
  Focus: Beta readiness: load tests, observability, error budgets, privacy reviews, app store prep.
- **Sprint 8:** `Aug 20, 2026` – `Sep 3, 2026`
  Focus: Release enablement: localization wave 1, support playbooks, GA switch, follow-up hotfix buffer.

Milestones:

- **M4:** Public GA launch with beta validation complete, store approvals, and support readiness (`Sep 3, 2026`)

Milestone Register

Milestone	Description	Target Date	Readiness Criteria	Status
M1	Core onboarding live with logging + retention enablers (goals &	`Jun 3, 2026`	FS-1..8 pass DoD; p95 dashboard < 2s	IN PROGRESS

	notifications) shipped with baseline metrics		baseline; event tracking active	
M2	Social engagement loops validated + leaderboard adoption driving retention uplift	Jul 3, 2026	≥10% weekly actives share; ≥30% weekly actives on leaderboard; +5% retention measured	NOT STARTED
M3	Macro insights live with adoption targets met + experience health and accessibility targets achieved	Aug 4, 2026	≥60% meal loggers view macro breakdowns; p95 < 2s on key views; AA accessibility checks pass	NOT STARTED
M4	Public GA launch with beta validation complete, store approvals, and support readiness	Sep 3, 2026	SLOs met; incident runbooks approved; load test pass; store approvals; support ready; comms live	NOT STARTED

Risks and Dependencies

- **Platform permissions (FS-4):** iOS/Android pedometer APIs and prompts. Mitigation: early device testing; clear UX copy; fallback handling.
- **Performance targets:** Dashboard p95 < 2s with real data. Mitigation: caching, lazy loading, perf budgets.
- **Social feature safety:** Abuse/spam vectors via sharing. Mitigation: rate limits, link safety checks.
- **Release readiness:** Store review and localization timelines. Mitigation: parallelize prep in Sprint 7.

Execution Checklist

- [ ] Define KPIs per milestone (activation, 7-day retention, DAU/WAU)
- [ ] Set observability dashboards and alerts for p95 targets
- [ ] Prepare release playbooks (beta and GA)
- [ ] Plan localization strings and review timeline (Sprint 8)
